



Service Items

Name	Description	Tier 1 Price	Unit Type	QTY	Taxable
Labor	See attached pages for details of work performed.	\$0.00	Hour	1	N

TOTAL*: \$0.00

* Not including taxes



Service Forms

Daily Form Fill out every day. even on PMs, and projects

TECH NAME Jacob Powell

DATE 03-11-2024

POINT OF CONTACT: Scott

DESCRIPTION OF WORK PERFORMED removed existing hot water heater and installed new instantaneous hot water heater on the wall. got new unit all piped in and checked for leaks. ran new drain line and gas line and tested the unit out to make sure it works. unit is running good at this time and cleaned up area before departure.

TOOLS USED hand tools, pipe cutter

MATERIALS USED OR PICTURE OF TAG* materials listed on toms daily

HOURS **REGULAR:**

OVERTIME:



Attachments





Service Items

Name	Description	Tier 1 Price	Unit Type	QTY	Taxable
Labor	See attached pages for details of work performed.	\$0.00	Hour	1	N

TOTAL*: \$0.00

* Not including taxes



Service Forms

Daily Form

Fill out every day. even on PMs, and projects

TECH NAME Tom Timlin
DATE 3/11/24
POINT OF CONTACT: Scott
DESCRIPTION OF WORK PERFORMED Removed and installed the new instantaneous water heater. got it all piped back in and checked for leaks, and all was good. Ran the drain and gas line to the new spots. Turned the unit on and set it up so it runs with the buildings recirculator pump. Unit is running good at this time.
TOOLS USED m18 propress
MATERIALS USED OR PICTURE OF TAG*
Copper
1: 1 1/2" to 1" reducer PP
1: 1x3/4x3/4" tee PP
3: 3/4" ball valves PP
6: 3/4" 90's PP
4: 3/4" st 90's
2: 3/4" unions PP
3: 3/4" female adaptors PP
1: 3/4" male adaptors PP
1: 3/4" Tee PP
1: 3/4 to 1/2" reducer PP
20': 3/4" type K copper

PVC
2: 3-2" sch 40 reducer
2: 2" st 90's
5': 2" pcv pipe
6: 3/4" 90's
2: 3/4" male adaptors
1: 3/4" female adaptor
1: 3/4" tee
20': 3/4" pcv pipe

Electrical
15': 12/2 BX wire
1: 2x4 electrical box
1: outlet
1: outlet cover

Gas line
2: 3/4" blk iron 90's
1: 3/4" blk iron cap
1: 3/4" blk iron tee
1: 3/4" blk iron union
1: 3/4" blk iron 1" to 3/4" bushing
2: 6" blk iron nipples
1: 5" blk iron nipple
1: 24" blk iron pipe
1: 54" blk iron pipe

HOURS
REGULAR:
OVERTIME:




Attachments

Title **File Name**


1000003496 03/11/2024
03:28 PM

ca69d7be-a94c-4e08-9a75-3aa32c6f41e0.jpg

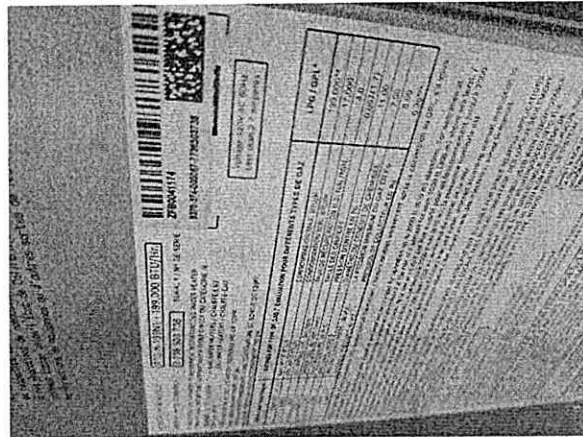


1000003499 03/11/2024
03:27 PM

f1155267-c8b3-46c7-b111-38252a5e1a51.jpg

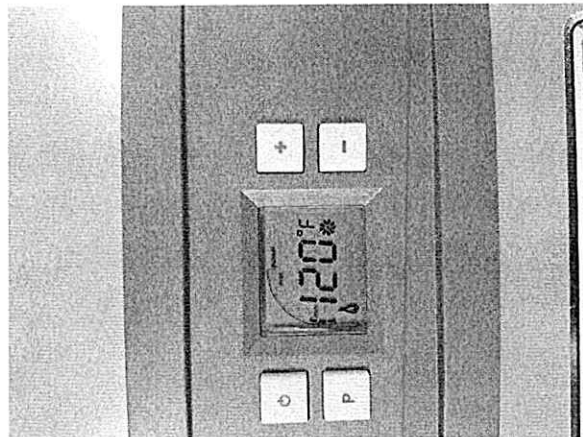


1000003498 03/11/2024
03:27 PM

175579c5-d9e2-4cc8-8fb4-08ad80f1333d.jpg

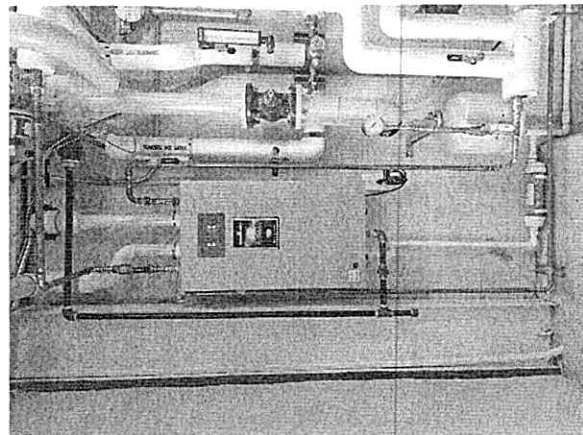

1000002723 03/11/2024
03:27 PM

100cd460-bf44-4e49-91bb-436c8a66768c.jpg

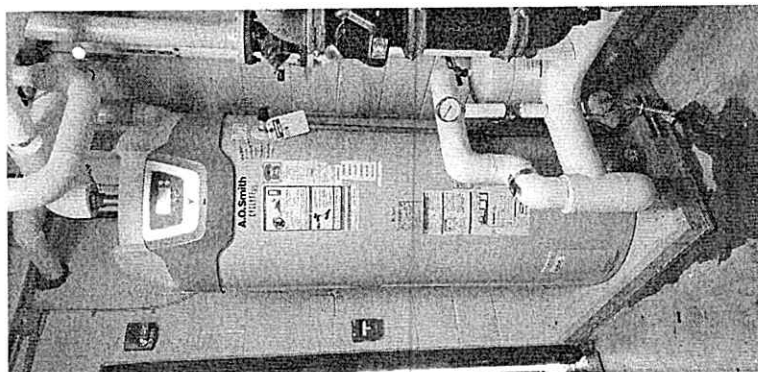

CERTIFICATION OF WORK

(To be completed by the Contractor and saved in the Contractor's CMMS)

FACID/Building USARC Fairview Date of Visit: 03-11-2024

Contractor Personnel on Site:

1. Jacob Powell
2. Tom Timlin

Work Performed:

Preventive Maintenance - Services Completed (Annual, Quarterly, Monthly, equipment identification, etc.)

1. Installed new hot water heater in outside garage.

Service Calls – Service Call Number and Description

1. CSS# 96148
2. CSS# _____
3. CSS# _____

CERTIFICATION OF WORK

To be signed by the Contractor:

Print Name: Jacob Powell Date: 03-11-2024

Signed: 

To be signed by Facility Manager:

By signing the Certification of Work, I certify that the above-named individuals representing the Contractor arrived on site and to the best of my knowledge, completed the stated work listed.

This is **NOT** a Certification that the Work was performed correctly – The COW simply verifies that that someone representing the Contractor was onsite and accomplished something

Print Name/Rank: _____ Date: _____

Signed: 

E-Mail: scott.w.kawski.civ@army.mil
