

**CERTIFICATION OF WORK  
SERVICE CALL**

(To be completed by the Contractor and saved in the Contractor's CMMS)

FACID/Building: VA006 Date of Visit: 11.18.2020

Contractor Personnel on Site:

- |                          |          |
|--------------------------|----------|
| 1. <u>Richard Walker</u> | 4. _____ |
| 2. _____                 | 5. _____ |
| 3. _____                 | 6. _____ |

**Service Call Number**

CSS# 27720 WO# 13303

**Description of Repairs**

found power had tripped, out boiler 1 low pressure switch.

and tripped boiler 2 low gas pressure Switch.

checked gas valve of b2 to ensure proper calibration, and checked pressure Switch to b1

adjusted demand, and waited for boilers to satisfy heat load. heat works, found leaking circulation pump, subbed to Moore's.

-----

**CERTIFICATION OF WORK**

To be signed by the Contractor:

Print Name: Richard Walker Date: 11.18.2020

Signed: 


To be signed by Facility Manager:

By signing the Certification of Work, the said government representative signature does not constitute acceptance of any work performed by the contractor, it only acknowledges that the contractor was on-site during the identified timeline:



Print Name/Rank: Don Huson Date: 11.18.2020

Signed: 

E-Mail: \_\_\_\_\_

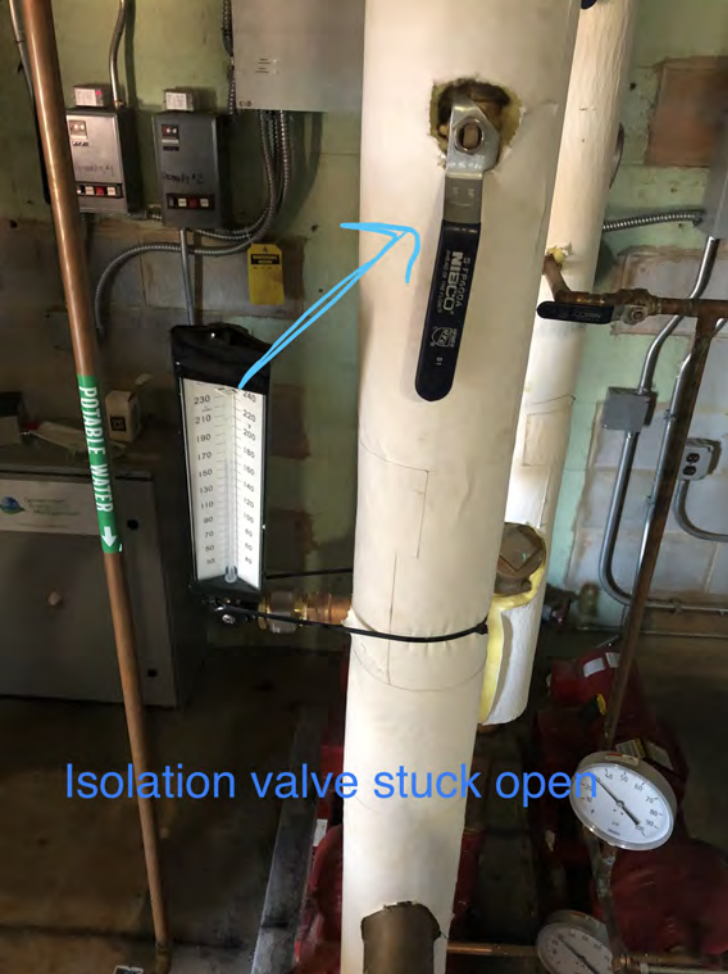

Isolation valve stuck open

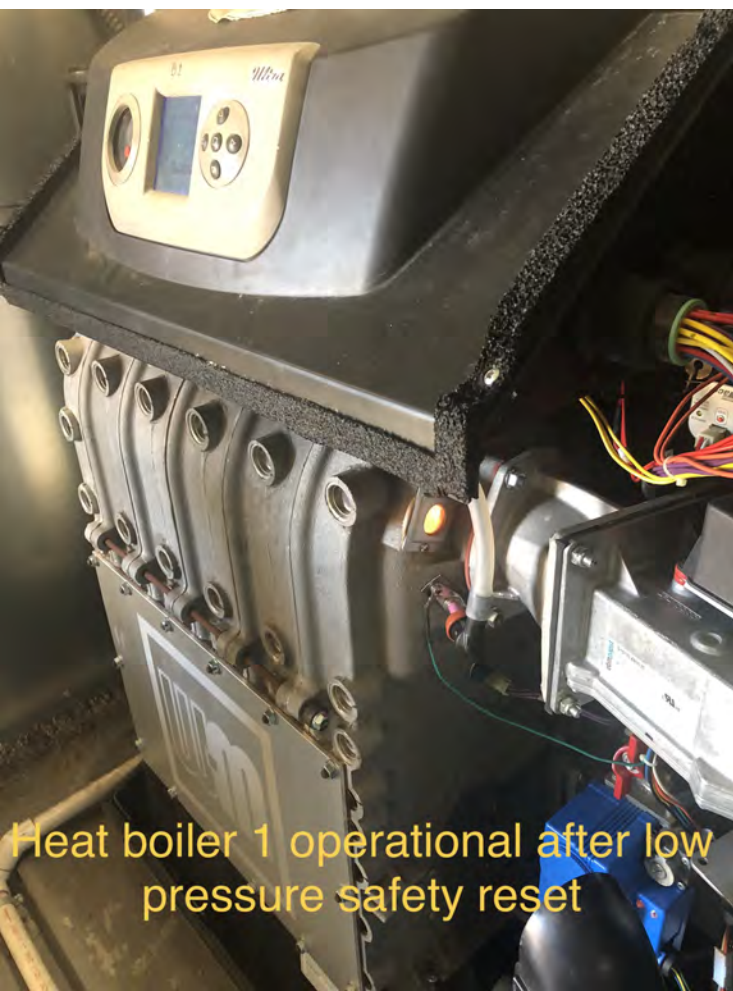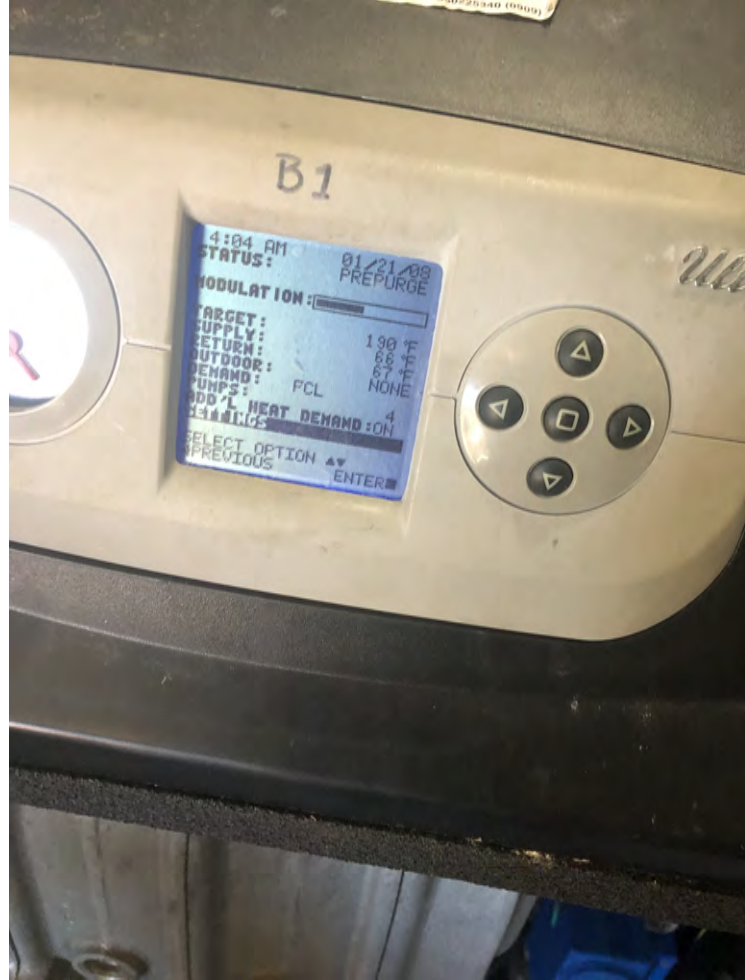

Heat boiler 1 operational after low pressure safety reset

