

**CERTIFICATION OF WORK
SERVICE CALL**

(To be completed by the Contractor and saved in the Contractor's CMMS)

FACID/Building: VA050 Date of Visit: 08/24/21

Contractor Personnel on Site:

- | | |
|----------------------|----------|
| 1. <u>JOSH CANTY</u> | 4. _____ |
| 2. _____ | 5. _____ |
| 3. _____ | 6. _____ |

Service Call Number

CSS# 31668 WO# 14665

Description of Repairs

Recovered refrigerant charge from system, pressurized with nitrogen and leak tested none were found. Blew nitrogen
nitrogen charge, installed both replacement low pressure switches replaced internals of TXV
as well as solenoid valve and placed system on vacuum until proper microns were achieved.
Cleaned work area and removed all tools and debris from work area before leaving site. This work order is complete

CERTIFICATION OF WORK

To be signed by the Contractor:

Print Name: Josh Canty Date: 8/24/21

Signed: *josh canty*

To be signed by Facility Manager:

By signing the Certification of Work, the said government representative signature does not constitute acceptance of any work performed by the contractor, it only acknowledges that the contractor was on-site during the identified timeline:

Print Name/Rank: CAPT. FRIEND Date: 8/24/21

Signed: GRENIER.SCOTT.AN
THONY.1007219551

Digitally signed by
GRENIER.SCOTT.ANTHONY.10072
19551
Date: 2021.09.02 14:18:22 -04'00'


E-Mail: _____









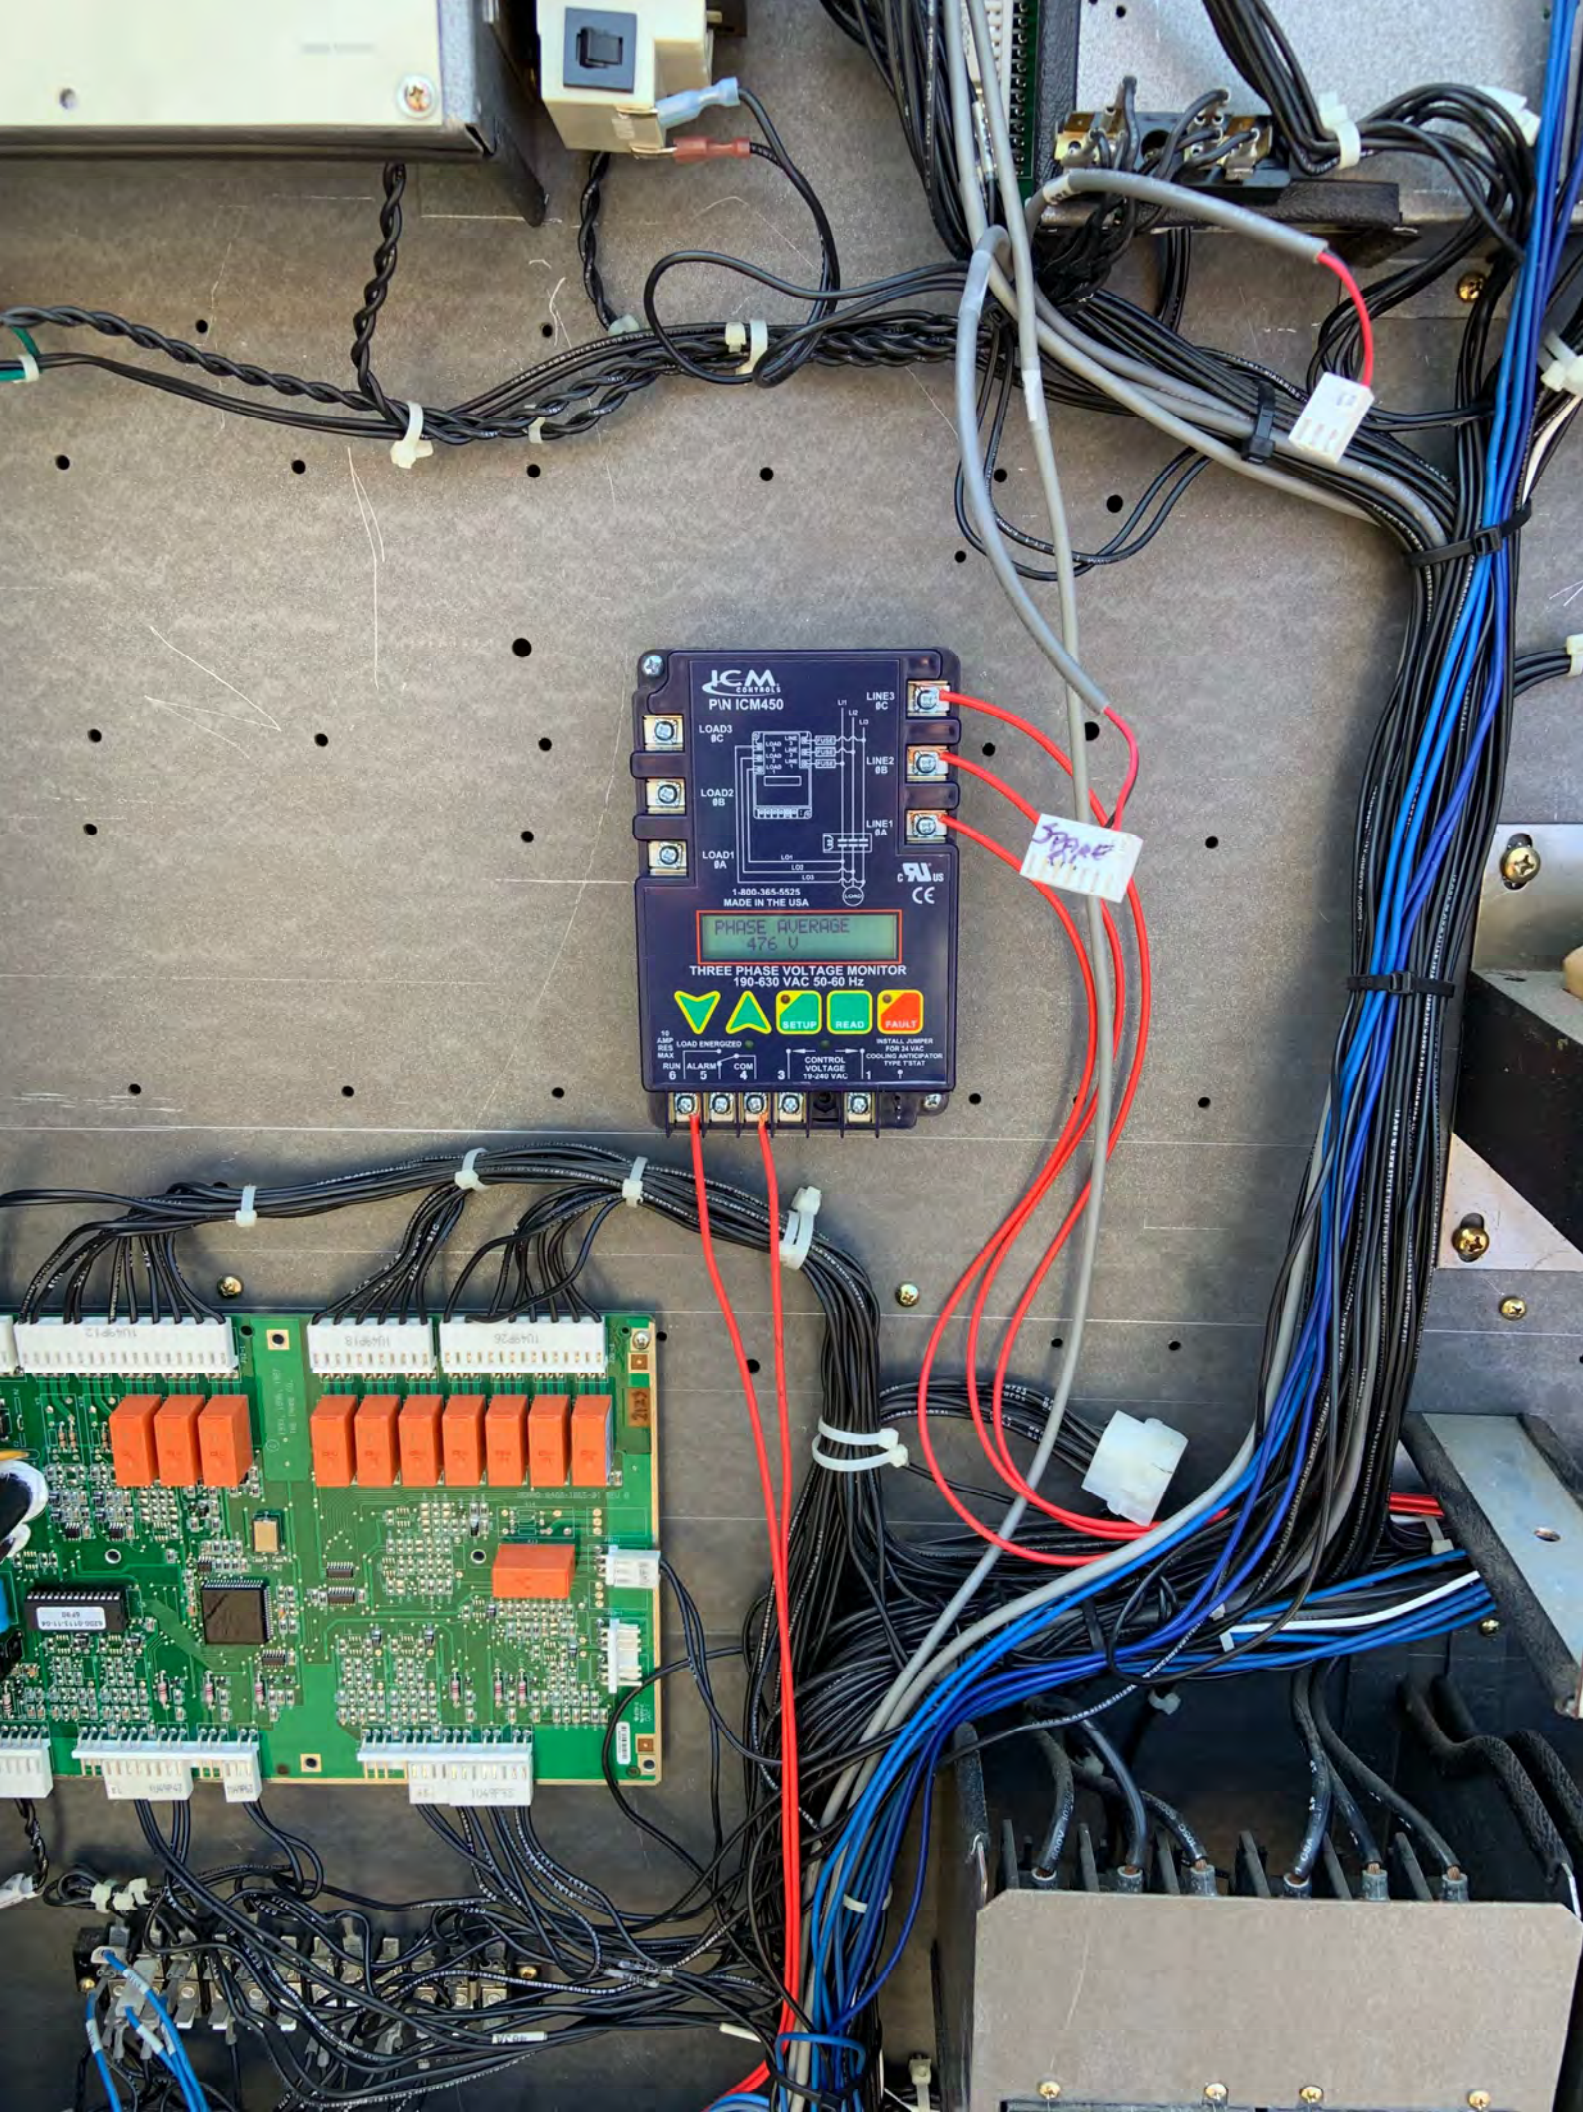

ICM
PIN ICM450

LOAD3 3C
LOAD2 3B
LOAD1 3A

LINE3 3C
LINE2 3B
LINE1 3A

1-800-365-5525
MADE IN THE USA

PHASE AVERAGE
476 V

THREE PHASE VOLTAGE MONITOR
190-630 VAC 50-60 Hz

10 AMP RES MAX RUN ALARM COM 3 CONTROL VOLTAGE 10-240 VAC 1

INSTALL JUMPER FOR 24 VAC COLOUR MATCH FOR TYPE T STAT
