

**CERTIFICATION OF WORK
SERVICE CALL**

(To be completed by the Contractor and saved in the Contractor's CMMS)

FACID/Building: VA 099 Date of Visit: 8.12.2020

Contractor Personnel on Site:

- | | |
|----------|----------|
| 1. _____ | 4. _____ |
| 2. _____ | 5. _____ |
| 3. _____ | 6. _____ |

Service Call Number

CSS# _____ WO# 12594

Description of Repairs

Found Evap flow sensor faulty. Ordered parts, picked up parts
From Richmond. Removed faulty parts. Installed new sensor/
Sequence-S-LED (BAC) cable. Tested chiller
operations. Chiller is cooling.

CERTIFICATION OF WORK

To be signed by the Contractor:


Print Name: Richard Walker Date: 8.12.2020

Signed: 


To be signed by Facility Manager:

By signing the Certification of Work, the said government representative signature does not constitute acceptance of any work performed by the contractor, it only acknowledges that the contractor was on-site during the identified timeline:

Print Name/Rank: Donald Hysen Date: 8.12.2020

Signed: 

E-Mail: _____

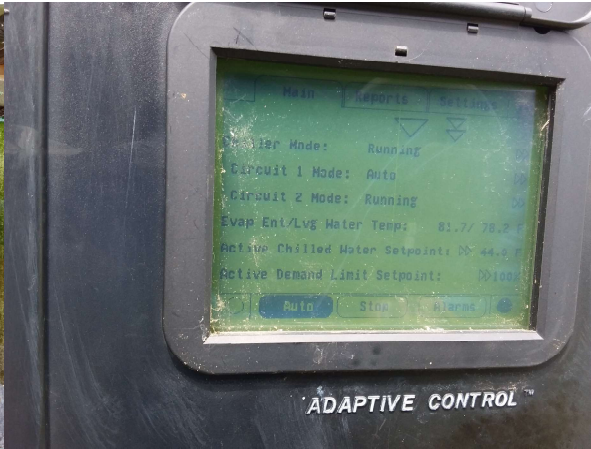

5-motion sensors

1-door keypad

no internal cameras

2-cages (LG magnetic door sensor on each cage)

1-LG magnetic sensor on vault door

No- vault lock change

1- dehumidifier inside vault (hard wired)

1-Advantor cabinet (2-7AH Batteries)
