


■ Customer Name :

Johnstown Transient
Quarters
Johnstown, PA

ASCO[®] Power
Services *Mission Critical Care*

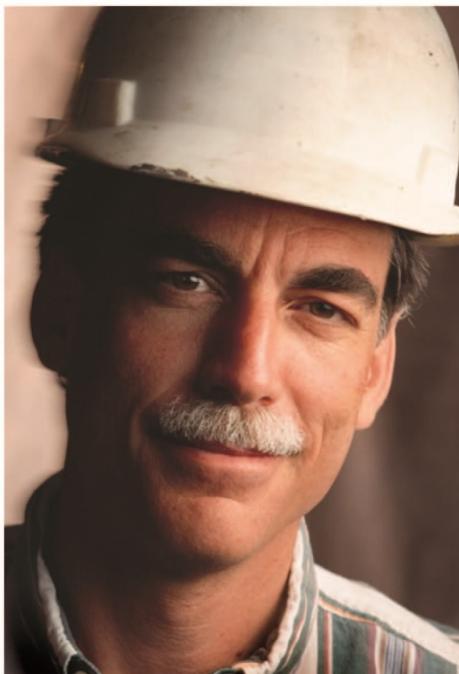

Activity : ASCO ATS Scheduled Maintenance

Dates : June 11, 2019



July 25, 2019

Johnstown Transient Quarters
Johnstown, PA

Dear Bernie Koblinsky,

We are pleased to provide you with this report of recent service work performed at your facility.

We understand you have a choice when it comes to Service. Thank you for choosing ASCO products & services for your critical application. We are constantly striving to make our organization the best.

Please feel free to contact us directly with comments & suggestions. Thank you for using ASCO Power Services.

Best Regards,

Your ASCO Power Services Team

Matt Miller
Account Representative
Office: (412) 431-9648

Dave Cowan
North Central District Service Manager
Office: (937) 642-1833
Mobile: (614) 477-8132



Summary

General Comments

ASCO Power Services dispatched a field service technician to perform a scheduled maintenance service. Inspected, cleaned, and recalibrated the equipment and found:

Specific Comments / Recommendations

- Test ATS periodically.
- Continue annual SM's to increase the life of the ATS.



Equipment List

Equipment ID	ATS 195 Hotel
Serial Number	248167 FP

Scheduled Maintenance Data Sheet

Service Date	06/11/2019	Catalog Number	G07ATSB32000C5XC		
BOM	750952	Voltage	208	Amperes	2000
Site Name	JOHNSTOWN TRANSIENT QTRS	Phase	3	CP Model	GP5
Street Address	195 AVIATION DRIVE	Frequency	60 Hz		
City, State, & Zip	Johnstown PA 15902	Arc Flash Rating - Cal	cal/cm^2 Not Labeled		
Service Order #	273992	Service Technician	Keith Eckert		
Mod Service Order #		Accessories	27		

Comments	LIVE INSPECTION OF ATS. CONTINUE SERVICE ON ATS
----------	---

Recommendations	
-----------------	--

Equipment ID	ATS 195 Hotel
Serial Number	248167 FP

Disable Engine Start	Yes
----------------------	-----

Bypass ATS	N/A	Isolate ATS	No
------------	-----	-------------	----

Settings		
Normal Source		
Voltage PU %	90	187.2 VAC
Voltage DO %	85	176.8 VAC
Freq PU %	95	57 Hz
Freq DO %	90	54 Hz
Overvoltage %		Disabled/Off
Rotation	Disabled/No	CBA
Emergency Source		
Voltage PU %	90	187.2 VAC
Voltage DO %	75	156 VAC
Freq PU %	95	57 Hz
Freq DO %	90	54 Hz
Overvoltage %		Disabled/Off
Rotation	Disabled/No	CBA
In-Phase Monitor	Enabled/Yes	

Timing		
Normal to Emergency		
Acc 1 override mom. outages	1	SEC
Acc 2B xfer to emergency	0	SEC
In sync	SEC	N/A
Fail to sync	SEC	N/A
Load Disconnect (DTTS)	SEC	N/A
Commit to Transfer	Disabled/No	
Emergency to Normal		
Acc 1F override mom. outages	0	SEC
Acc 3A xfer to normal - test	30	SEC
Acc 3A xfer to normal - fail	30	MIN
Acc 2E Engine Cooldown	5	MIN
Phase Voltage	A-B	B-C
Normal Voltage	212	212
Emergency Voltage	205	205
Record Generator Start Vc	5.58	VDC
Generator Frequency	60.01 Hz	
Connected	A-L	B-L
Record Normal mV Drop	**	**
Emergency mV Drop	**	**
Temperature Readings		
Connected To Normal	A	79
Connected To Emergency	A	79
Ambient	76	All Readings In F

Control Panel Data		
Software Vers.	32	
Total Transfers	160	
FailTransfers	42	
Days Energized	5487	
Baud Rate	N/A	
Address		
Accessory Timing		
Acc 31F N>E Pre	0	SEC
Acc 31M N>E Post	0	SEC
Acc 31G E>N Pre	0	SEC
Acc 31N E>N Post	0	SEC
Acc 2C		SEC

Equipment ID	ATS 195 Hotel
Serial Number	248167 FP

Contact Inspection	Stationary Contacts			Moveable Contacts		
	A	B	C	A	B	C
Emergency Main Contact	N/A	N/A	N/A	N/A	N/A	N/A
Emergency Arcing Contact	N/A	N/A	N/A	N/A	N/A	N/A
Normal Main Contact	N/A	N/A	N/A	N/A	N/A	N/A
Normal Arcing Contact	N/A	N/A	N/A	N/A	N/A	N/A

Contact Resistance	A-L	B-L	C-L	N-L
ATS Normal	LIVE	LIVE	LIVE	N/A
ATS Emergency	LIVE	LIVE	LIVE	N/A
Bypass Normal	N/A	N/A	N/A	N/A
Bypass Emergency	N/A	N/A	N/A	N/A

All contact resistance readings listed in micro-ohms

E-Excellent; S-Satisfactory; P-Poor

Coil Resistance in Ω	TS Coil	Dual Operator N	Dual Operator E
Primary	2.4 Ω	N/A Ω	N/A Ω
Secondary	2.5 Ω	N/A Ω	N/A Ω

Coil Resistor in Ω
N/A Ω

Serviceable Items Checklist			
Live	All relay contacts under 1 ohm	Live	Switch operates manually without binding
Live	TS Control and Aux Contacts under 1 ohm	N/A	9-Volt battery replaced (Group 1 CP only)
Live	Check TS Control and Contact linkage adjust	Live	Cubicle/cabinet vacuumed and wiped clean
Live	Clean main contacts on emergency side	Live	Rectifier in good condition
Live	Clean arcing contacts on emergency side	N/A	Bypass power supplies function properly
Live	Clean main contacts on normal side	Live	Evidence of thermal damage
Live	Clean arcing contacts on normal side	Live	Temp Variance >25F on current carrying parts
Live	Check wiring & cable connections for tightness	Live	Evidence of therm damage to insulating parts
Live	Lubricate coil, cam, & linkage	Live	Evidence of moisture on insulating parts

Verify ATS Not Isolated	Yes	Verify ATS Bypass In Auto	N/A	Verify Engine Start Connected	Yes
-------------------------	-----	---------------------------	-----	-------------------------------	-----

Record Normal mV Drop	A-L	**	B-L	**	C-L	**	Record Generator Start Voltage	5.4	VDC
-----------------------	-----	----	-----	----	-----	----	--------------------------------	-----	-----
