



Date: 10/13/2023
Facility ID: PA118
Work Order # 14024
Boiler ID 6560




Seasonal Start Up - Boiler PM Inspection Worksheet

1. Verify full boiler
2. Test the safety/relief valve after startup (full pressure test)
3. Clean or replace the fuel filters
4. Clean the fuel nozzles
5. Inspect, clean and functionally test the flame scanner and flame safeguard relay
6. Clean and adjust the ignition electrode
7. Replace the vacuum tube in flame safeguard control, if applicable
8. Perform pilot turn down test
9. Verify proper water flow through the boiler
10. Perform visual combustion test and adjust the burner for maximum efficiency
11. Test all safeties to verify burner shutdown

INSPECTION NOTES:

Tested safety switches tested relief valve Tested both vacuum switches removed igniters and

Cleaned

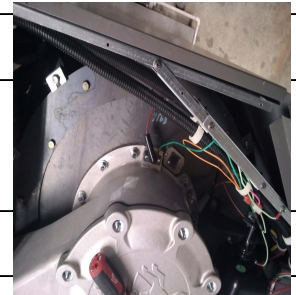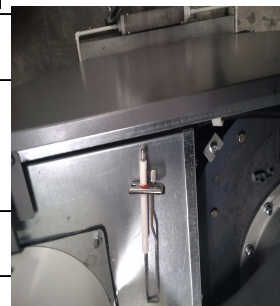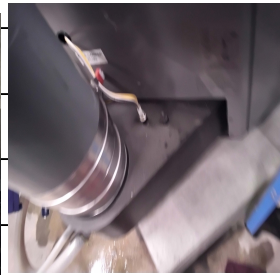

CSS TICKETS NEEDED:
