

**CERTIFICATION OF WORK
SERVICE CALL**

(To be completed by the Contractor and saved in the Contractor's CMMS)

FACID/Building: VA49

Date of Visit: 1/24/22

Contractor Personnel on Site:

1. Peter Langsta

4. _____

2. Paul Isom

5. _____

3. _____

6. _____

Service Call Number

CSS# 34099

WO# 15980

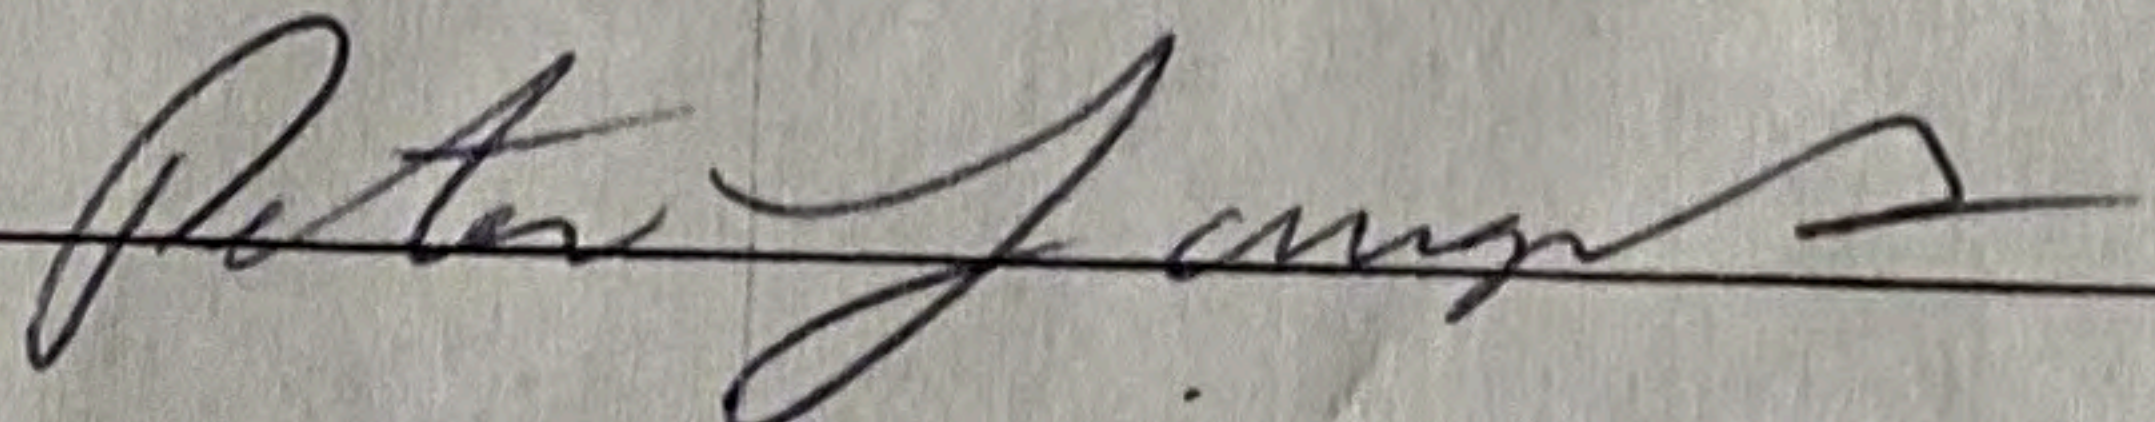
Description of Repairs

Performed Boiler maintenance on 4 Alpha boilers
in the Mech Room

CERTIFICATION OF WORK

To be signed by the Contractor:

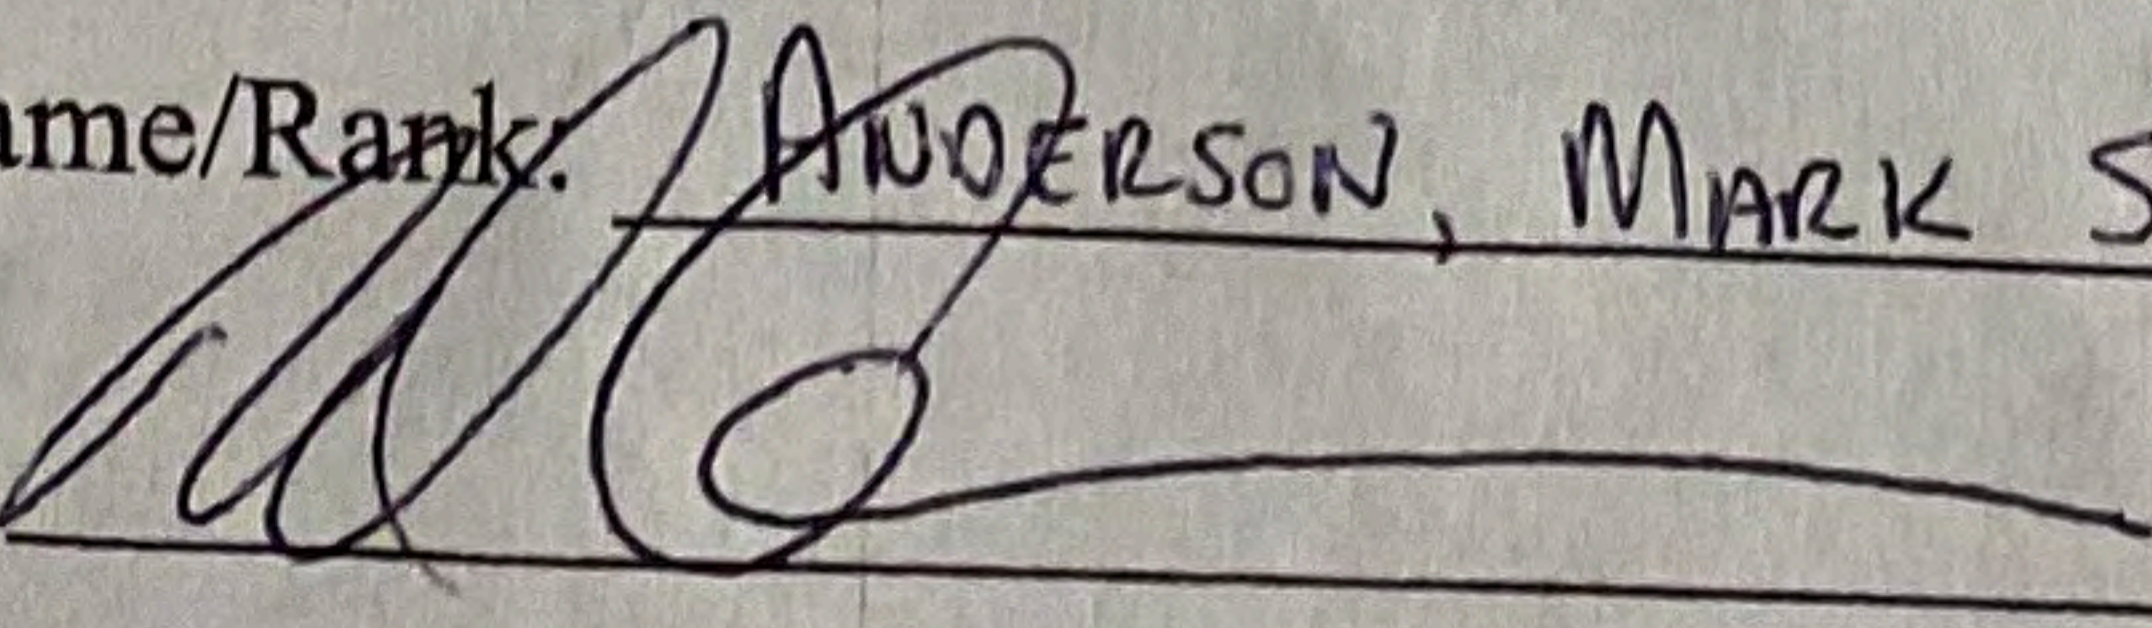
Print Name: Peter Langsta Date: 1/24/22

Signed: 

To be signed by Facility Manager:

By signing the Certification of Work, the said government representative signature does not constitute acceptance of any work performed by the contractor, it only acknowledges that the contractor was on-site during the identified timeline:

Print Name/Rank: ANDERSON, MARK S., GS-12 Date: 24 JAN 22

Signed: 

E-Mail: mark.s.anderson7.civ@army.mil



Proudly serving the entire states of Virginia & North Carolina.

Altavista, VA • Charlottesville, VA • Chesapeake, VA • Manassas, VA
Lynchburg, VA • Richmond, VA • Raleigh, NC • Charlotte, NC

P.O. Box 119 • Altavista, VA • 800.789.7199 • service@mooreselectric.com

Billing Address	Site Address
Customer: TIDEWATER, INC Address: 6625 SELNICK DRIVE ELKRIDGE MD 21075 Phone: 614-623-9569	Customer: USARC VA049 CHESTERFIELD Address: 6700 STRATHMORE ROAD NORTH CHESTERFIELD VA 23237 Phone: 614-623-9569
Service Call #: COM0170839	Call Type: COM-HVAC

Service Requested
WO: 15980 NTE: 450.00 SOW: Boilers #1 ,#2, #3 ,#4 fires sides need to be cleaned 1/12/22AC: WAITING FOR SCHEDULE DATE 1/14/21AC: CUSTOMER IS REQUESTING QUOTE TO CLEAN ALL FIRES SIDES ON BOILER 1,2,3,4 1.14.22: Quote submitted. Technician will source materials needed. 1/24/22AC: QUOTE APPROVED 2 MEN 12 HOURS EACH 2,935.00

Problems					
Description	Tech	Equip. Desc and Model	Manufacturer	Equip. Serial	Asset ID
TROUBLE SHOOT UNIT	PETELANGST	PM for all 4 boilers	Burnham		
TROUBLE SHOOT UNIT	JARRATISOM				

Tech Notes
Site Start - 1/24/2022 8:00 AM Site Stop - 1/24/2022 6:30 PM Arrived at shop to pick up shop vac and tools for boiler pms. Drove to site checked in with base police. Drove to va49. Unloaded all tools by back door. Parked truck and called site contact to get access. Went mech room. Found boilers and started pm on each boiler. Used shop vac and brush to clean the combustion chamber. On unit #4 found the burner plate insulation was cracked and when I pulled the the burner out it fell off. Also found the back insulation has talked and was not used able. Called manufacture to get ultimate parts numbers and called supply house to see if parts are available . Finished the pm on the 3 other boilers. Started and checked operations. They are running and maintaining temp at this time. Will quote repairs to unit 4. Left power and gas off to 4. Got COW signed before staff left. Job is complete

Labor			
Date	Technician	Description	Hours
1/24/2022	PETER LANGSTON	REGULAR HVACR LABOR	10.50
1/24/2022	PAUL ISOM	REGULAR HVACR LABOR	4.50

Materials			
Date	Part Number	Description	Quantity
1/24/2022	CMISCX-TRUCK CHARGE	TRUCK CHARGE	1.000
1/24/2022	CMISCX-TRIP CHARGE	TRIP CHARGE	1.000
1/24/2022	CMISCX-QUOTED GS AMOUNT	QUOTED AMOUNT SUBMITTED FOR THIS GENERAL SERVICE JOB	24.000
1/24/2022	CMISCX-SOOT VACUUM FEE	SOOT VACUUM FEE	1.000
1/24/2022	CPVCCP-PIPE DOPE CAN	PIPE DOPE CAN	1.000

Signed By	No one to sign	Signature	no one to sign	Date	1/24/2022
------------------	----------------	------------------	----------------	-------------	-----------









