


Additional Funding Request


PA118	CSS# 17689 WO# 7597 Asset# 6724											
Description of Repairs	Labor and materials to remove, and install a new air compressor electric motor											
Diagnosis: Initial Work Order	Compressor in Warehouse is not working. It does not turn on at all. Breaker is not tripped, and resetting it does nothing. There is an auto/manual switch on the compressor itself, neither modes turn it on.											
Diagnostic Fee	\$ 240.00 Renick Brothers \$120/hr x 2											
Additional Labor Cost to Perform Repairs	\$ 800.00 Renick Brothers \$120/hr x 2 Travel 40 miles @\$1/mile \$80											
Additional Material Cost to Perform Repairs	\$386.90 <table border="1"><tr><td>B384 Electric motor \$ 365.00</td><td>1</td><td>\$365.00</td><td>\$365.00</td></tr><tr><td>Sales Tax</td><td></td><td></td><td>\$21.90</td></tr></table>				B384 Electric motor \$ 365.00	1	\$365.00	\$365.00	Sales Tax			\$21.90
B384 Electric motor \$ 365.00	1	\$365.00	\$365.00									
Sales Tax			\$21.90									
Total Cost of Repair	\$ 1,426.90											

020812485

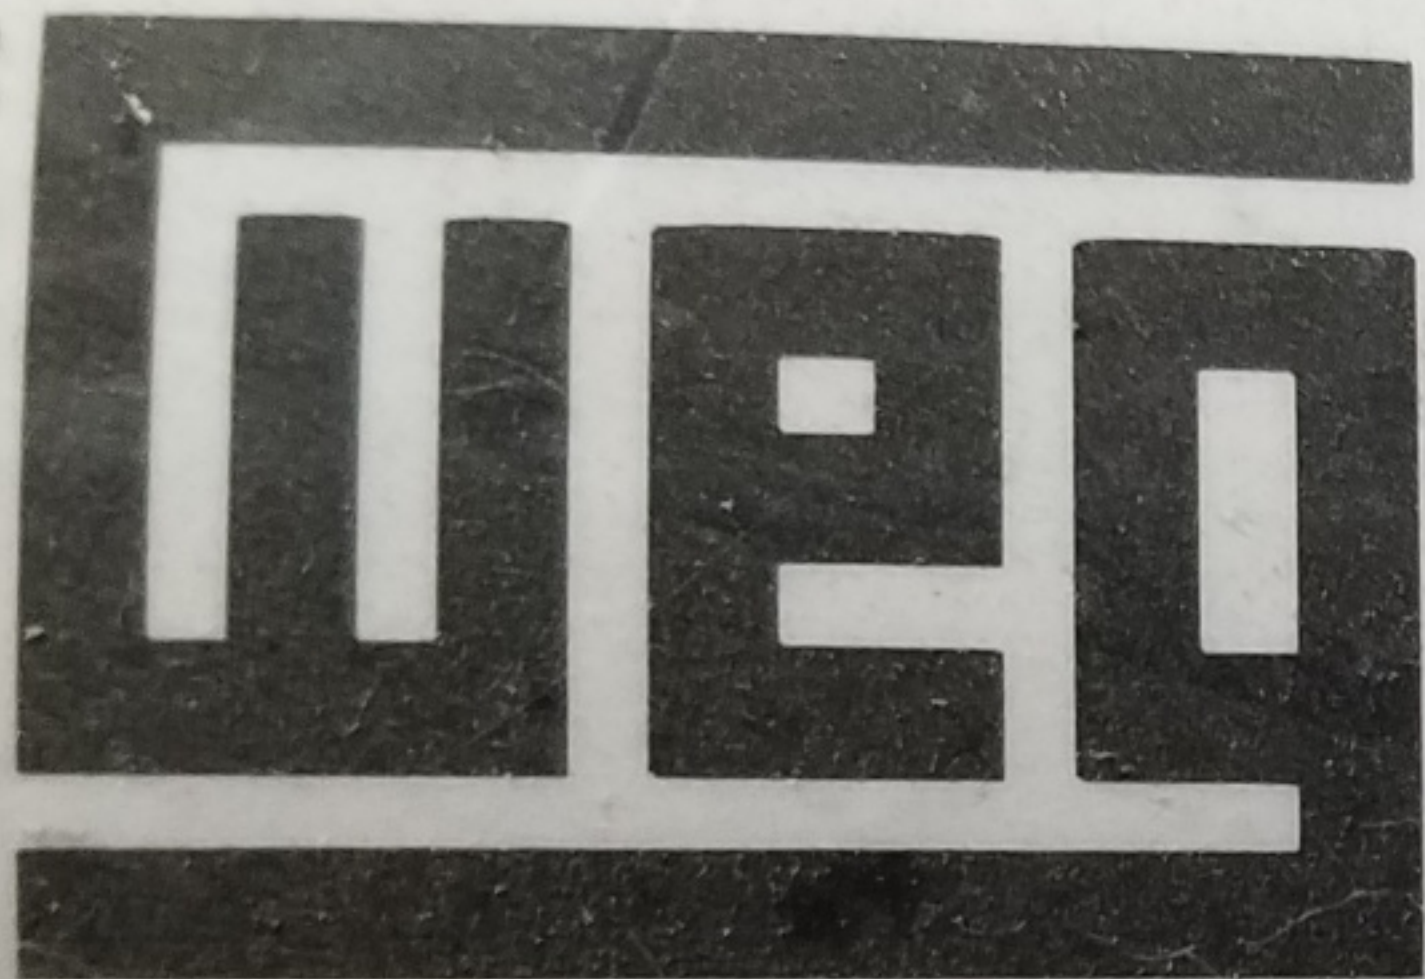

MADE IN BRAZIL

15FEV05



LR38324

THERMALLY PROTECTED

PART # D26719

MOD.1UMOIC4NXX6.402E

PH 1 | 182/4Y

RPM 3450

240 V

23.0 A

DUTY CONTINUOUS

60 HZ

SF 1.00

INS F

AMB 40°C

ENCL OPEN

1
L1

4
L2

1-BLUE 4-YELLOW

For On-Site Service

DO NOT RETURN TO PLACE OF PURCHASE
For details or to arrange for service repair

Call 1-888-559-8550


Mod. CPLKC7080V2-1

Gal.

80V

**HP/CV
PEAK**

--



LISTED

721Y AIR
COMPRESSORS
E73870

**Displacement
Desplazamiento / Alésage**

20.2 CFM

**Air Delivery (SCFM)
Despacho Aéreo (SCFM)
Debit d'air (pi³-mn standard)**

17.3 SCFM @ 100 PSI

16.8 SCFM @ 175 PSI

Electr.

240V/30A/60HZ/1PH

Pump / Bomba / Pompe

D26167

Max Pres / Pres Máx

175 PSI

Max. R.P.M. / RPM Máx. / T.p.M.

1200 RPM D26163

SER. NO. 2503020225



200530-2

CALIFORNIA CODE 462 (1)(2)

**COMPLIES TO
STANDARD NO. HACA 100**

**PORTER-CABLE CORP.
JACKSON, TN 38302
1-888-559-8550**
