

**CERTIFICATION OF WORK
SERVICE CALL**

(To be completed by the Contractor and saved in the Contractor's CMMS)

FACID/Building: WV022 Date of Visit: 04/03/2026

Contractor Personnel on Site:

- | | |
|---------------------------|----------|
| 1. <u>Michael Bennett</u> | 4. _____ |
| 2. _____ | 5. _____ |
| 3. _____ | 6. _____ |

Service Call Number

FEMS# 3535924 WO# 21646

Description of Repairs

Inspected heat exchanger for cracks or leaks, no leaks found, will return to do combustion analysis for boiler #2.
Verified operations of pump, ran in hand mode for a few hours, no signs of failure, will reverify while performing combustion analysis.

CERTIFICATION OF WORK

To be signed by the Contractor:

Print Name: Michael Bennett Date: 04/03/2026

Signed: 



To be signed by Facility Manager:


By signing the Certification of Work, the said government representative signature does not constitute acceptance of any work performed by the contractor, it only acknowledges that the contractor was on-site during the identified timeline:

Print Name/Rank: Andrew Rodeheaver Date: 04/03/2036

Signed: 

E-Mail: andrew.b.rodeheaver.mil@army.mil

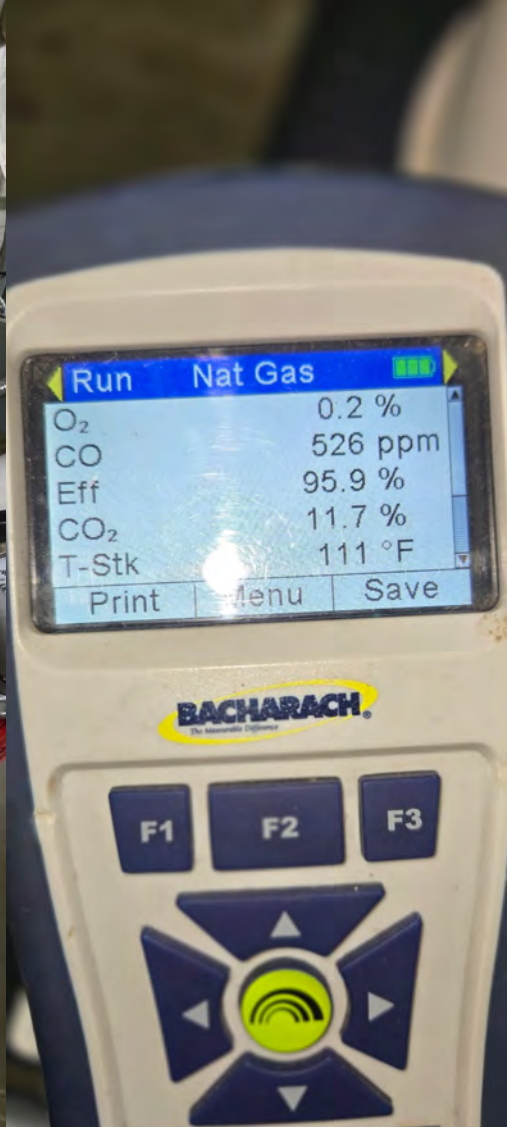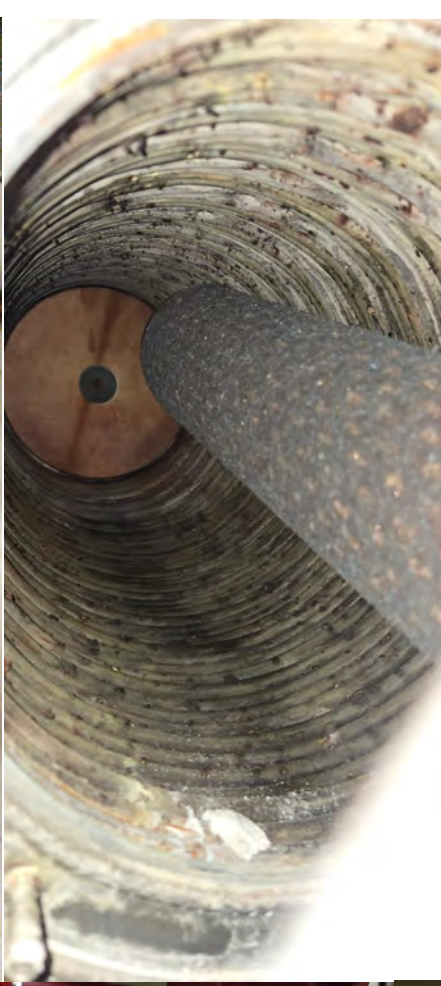

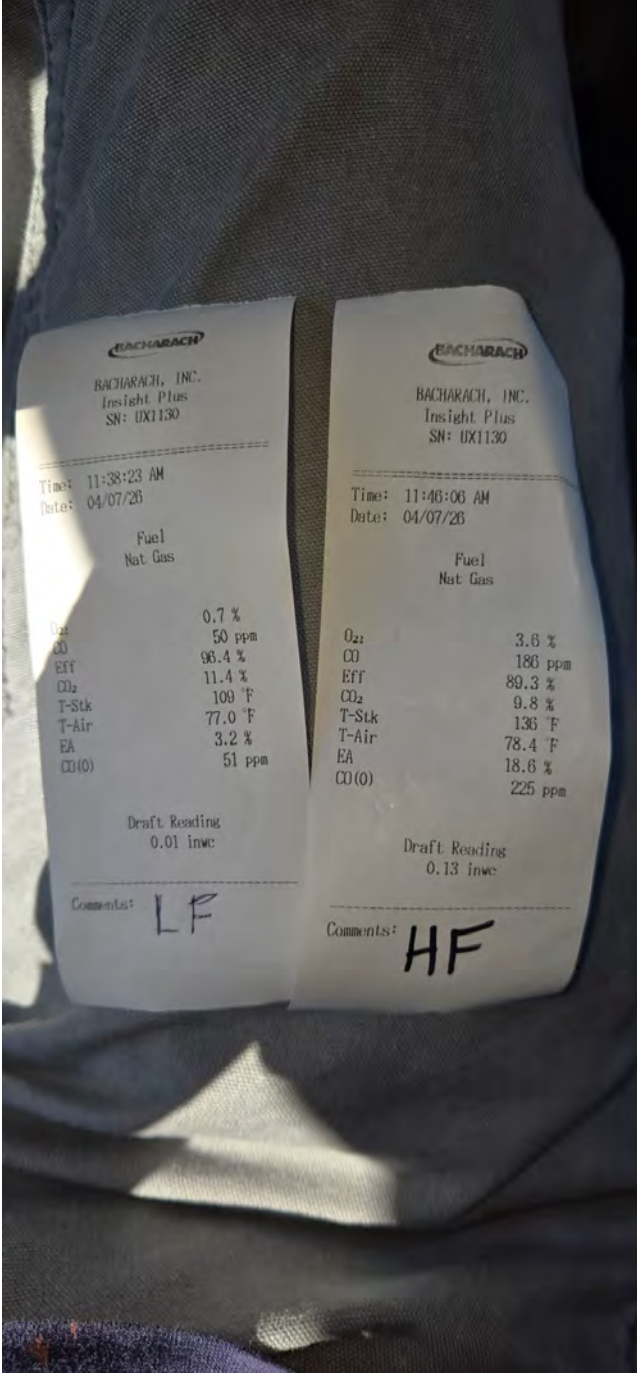

BACHARACH, INC.
Insight Plus
SN: UX1130

Time: 11:38:23 AM
Date: 04/07/26

Fuel
Nat Gas

O ₂	0.7 %
CO	50 ppm
Eff	98.4 %
CO ₂	11.4 %
T-Stk	109 F
T-Air	77.0 F
EA	3.2 %
CO(O)	51 ppm

Draft Reading
0.01 inwc

Comments: LF

BACHARACH, INC.
Insight Plus
SN: UX1130

Time: 11:46:06 AM
Date: 04/07/26

Fuel
Nat Gas

O ₂	3.6 %
CO	186 ppm
Eff	89.3 %
CO ₂	9.8 %
T-Stk	136 F
T-Air	78.4 F
EA	18.6 %
CO(O)	225 ppm

Draft Reading
0.13 inwc

Comments: HF
