

PREVENTATIVE MAINTENANCE PROGRAM CHECKLIST

THERMOSTATS

REVIEWED

By Mike Merchan at 8:50 am, Apr 09, 2019

SITE AND BLDG #: WV002-01

MECHANIC

SIGNATURE: *Andy Bird*

DATE: 4-8-19

LOCATION/RM #:

START TIME: 7:30AM

FINISH TIME: 12PM

Site Location	WO #	Asset #	PM #	Manufacturer	Model Number	Serial #	Asset Description	Asset Location
WV002-01	8315	6221		Trane	N/A		J-1502000-17 24-pc ThAn129,1A,103,1B,127,130,1K,106,108,122,1J,123,121,119,113,112B,112A,112,117,118	Through out
WV002-01	8315	6329		Trane	N/A		J-1502000-17 42-pc Thermostat Analog Throughout	Throughout
WV002-01	8315	6343			N/A		J-1502000-17 4-pc Thermostat Analog Rm 152, 135, 106,124	✓
WV002-02	8253	5404					J-1502000-17 1-pc Thermostat Analog	✓
WV002-02	8253	5516		Honeywell	N/A		J-1502000-17 1-pc Thermostat Analog	✓
WV002-02	8253	6268		Trane			J-1502000-17 2-pc Thermostat Analog Rm 100, 103	RM 100
WV002-02	8253	6338		Honeywell	N/A		J-1502000-17 4-pc Thermostat Analog Rm 106, 101A, 102,103	✓




CHECK POINT	CHECKPOINT DESCRIPTION	TASK COMPLETE		NOTES/ ACTIONS (IF TASK COMPLETE IS CHECKED NO, PROVIDE EXPLANATION)
		YES	NO	
SPECIAL INSTRUCTIONS				
1	In addition to the procedure(s) outlined in this standard, the equipment manufacturer’s recommended maintenance procedure(s) and/or instruction(s) shall be strictly adhered.	✓		
2	Always follow lock out/tag out procedures. De-energize or discharge all hydraulic, electrical, mechanical, or thermal energy prior to beginning work.	✓		
TO BE PERFORMED AT EACH INSPECTION SERVICE				
1	If EMS (Energy Management System) If it is EMS controlled 1- We log into computer with user name and password for EMS or DDC obtained from site personnel. 2- Validate set point and actual temp at computer	✓		
2	Review all zone set points at the server IF Applicable	✓		
3	Inspect thermostat installation; ensure mounting is correct, fastened secure and that the thermostat is not blocked by equipment generating heat or furniture blocking air circulation.	✓		

4	Remove thermostat cover and lightly blow away any accumulated dust with canned low-pressure air.	✓		
5	If applicable, replace battery as needed.	✓		
6	Use our own Temperature meter to validate the computer is correct. If it is not EMS or DDC controlled take our temperature meter and check against actual thermostat and record temperature	✓		

Note: The technician shall perform any repairs identified during PM up to \$250 (direct labor and direct material cost) per PM occurrence. For any deficiencies found exceeding \$250 open a corrective maintenance (CM) ticket and include the Asset #, WO #, photos, and a detailed description of the deficiency.

To be performed by: HVAC Technician

Additional Notes:

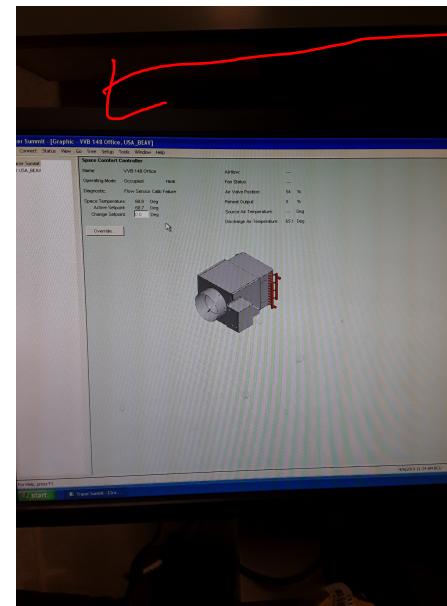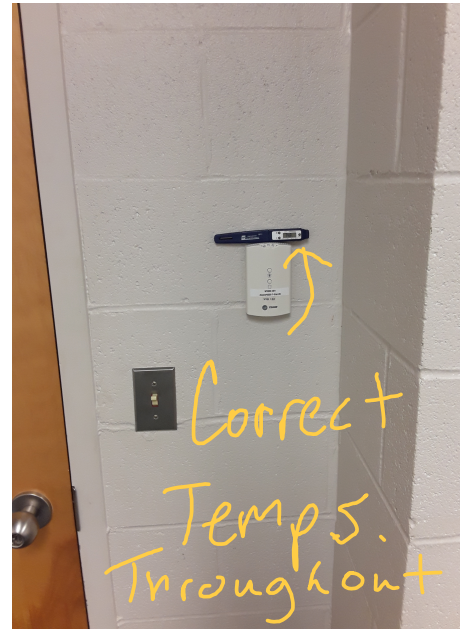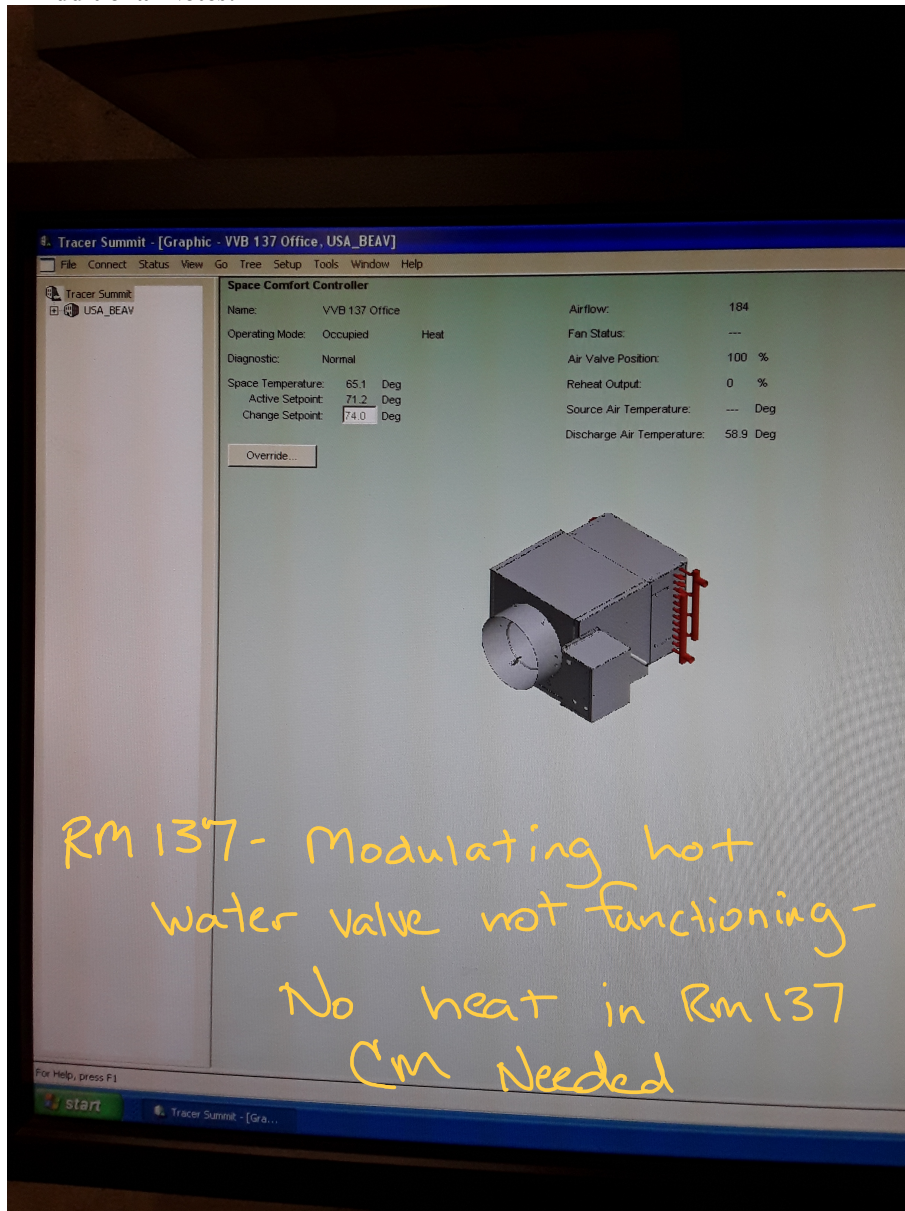

RM 148 (AFOS)
Ms. Ramsey's Rm
has failed Flow
sensor Calib failure,
CM Needed
