

Region: 2

Location: NY127

CSS #: 24591

Maximo Work Order No.: 7916

Asset #: 190917-636

Date Issued: 3/20/20

Original Description:

Hot water leaking in Mechanical Room 114

Repairs Needed:

Labor and materials to replace leaking hot water pump HWP-1-T.

Note 4 week lead time for pump.

RS Means Line Buildup and Labor Summary (Data Version 2017, Q4):

Quantity	Line Item Number	Description	Labor Hours	Labor Rate/Hr	Materials	Equipment	Total
--	NA	Materials (See attached detail)	--	--	\$2,952.77	--	\$2,952.77
--	NA	Tidewater Labor (Diagnostic and Repair)	13	\$80.00	--	--	\$1,040.00

Estimate Summary:

Labor Hours	Labor Cost	Material Cost	Equipment	Total Cost	CE Factor	Total Estimate
13	\$1,040.00	\$2,952.77	\$0.00	\$3,992.77	103%	\$4,112.55



WORK ESTIMATE

CSS #: 24591

Work Order #: 7916

Emergency ☐

Urgent ☒

Routine ☐

Company Name:	Tidewater, Inc.	Facility ID:	NY127
Contractor POC:	Adam Colopy		
Telephone No:	740-819-6207	Building/Location; (e.g., Classroom/Room #)	Mech
E-Mail Address:	adam.colopy@tideh2o.net		
Assigned Technician(s):	Patrick Brown		

DESCRIPTION of WORK and EXPLANATION for REPAIRS or REPLACEMENT

Labor and materials to replace leaking hot water pump HWP-1-T.

Note 4 week lead time for pump.

LABOR/MATERIAL		MATERIAL/ SUB UNIT DOLLAR AMOUNT	LBR/HR \$80	LINE ITEM TOTAL DOLLAR AMOUNT
ITEM	QUANTITY			
Labor			8	\$640.00
Armstrong Pump ASG4280	1	\$2,702.87		\$2,702.87
Freight Shipping	1	\$250.00		\$250.00
Diagnostic Labor			5	\$400.00
SUB-TOTAL COSTS:		Materials Total	\$2,952.87	Labor \$1,040.00
TOTAL			\$3,992.87	

F.W. Webb Company
6792 Townline Road
Syracuse, NY 13211
TEL# (315-476-9322)
FAX# (315-472-4139)

Quote
Number
03/27/20 66843782

To:

TIDEWATER, INC.
6625 SELNICK DRIVE

SAME
6792 Townline Road

ELKRIDGE MD 21075

SYRACUSE, NY 13211

(410-540-8700) Fax# (410-579-1685)

Cust #	Customer Po#	Rel#	Writer	Date Req
198314	ARMSTRONG PUMP		BTW	03/27/20

PAGE 1 OF 1

Quoted By: BRIAN WOLFORD

Quantity	Description	Net Price	Exten	Ln#
1	#ARMSTRONG CIRC PUMP 3HP 3P + ASG42802X1X104P (S3873215) 4 WEEKS ARO PLUS FRT	2111.620	2111.62	(1)

Sub Total: 2111.62
Total: 2111.62

*** NUMBER OF DAYS QUOTE VALID IS 10 ***

PLEASE REFERENCE QUOTE # 66843782 FOR INQUIRIES OR ORDER OF ABOVE MATERIAL

+ THIS PRODUCT IS A SPECIAL ITEM. RESTOCKING FEES MAY APPLY.

ARMSTRONG



MODEL NO.

2x1x10

42280

CONSTRUCTION

BF-STD

PUMP CAPACITY

48

US
gpm

85

ft

SERIAL NO.

G 745133

MOTOR

3

hp

1800

rpm

MAX. PRESS. MAX. TEMP.

175

psi

250

°F

MAX. FREQ. TAG

60

Hz

HWP-11 REV

ARMSTRONG PUMPS INC.
NORTH TONAWANDA, N.Y.
406912-100

S.A. ARMSTRONG LIMITED
TORONTO, ONTARIO


www.armstrongpumps.com

Product of Canada

ARMSTRONG


EXPERIENCE BUILDING...

18MAR13 1018974010 11300618

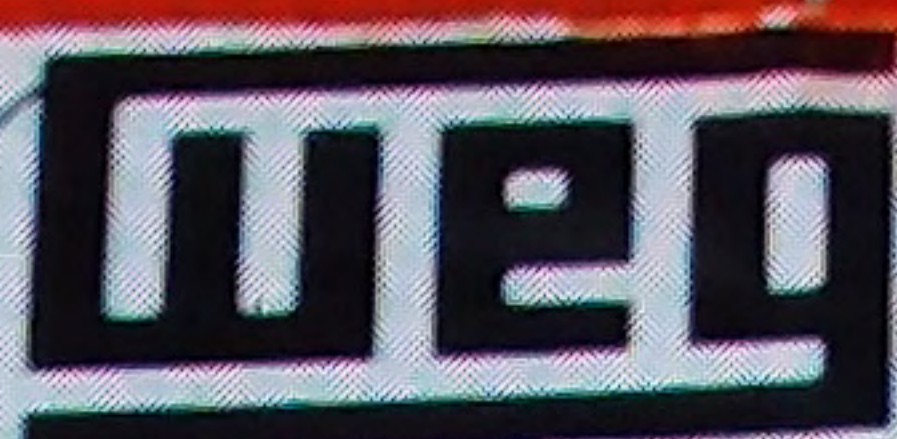

MODEL 00318OP3E182JM
MOD. T00IC0X0H0000302084

PH 3	182.5A	HP (kW)	3.0x3.20
RPM	1760	OUTY	CONT
230/480 V		RS HE	SP 1.15
8.08/4.04 A		INS FAT 80 F	AMB 40 C
SFA		ENCL ODP	SP 0.79
EFF% 86.5%		DES B	IP 21
		TYPE DP	CODE J
1/2-2 3HP 190/380V 2.82/4.21A 1450RPM SF1.00			
<div><div><div>T4</div><div>T5</div><div>T6</div><div>T7</div><div>T8</div><div>T9</div><div>T1</div><div>T2</div><div>T3</div><div>L1</div><div>L2</div><div>L3</div></div><div>LOW VOLTAGE</div></div> <div><div><div>T4</div><div>T5</div><div>T6</div><div>T7</div><div>T8</div><div>T9</div><div>T1</div><div>T2</div><div>T3</div><div>L1</div><div>L2</div><div>L3</div></div><div>HIGH VOLTAGE</div></div>			

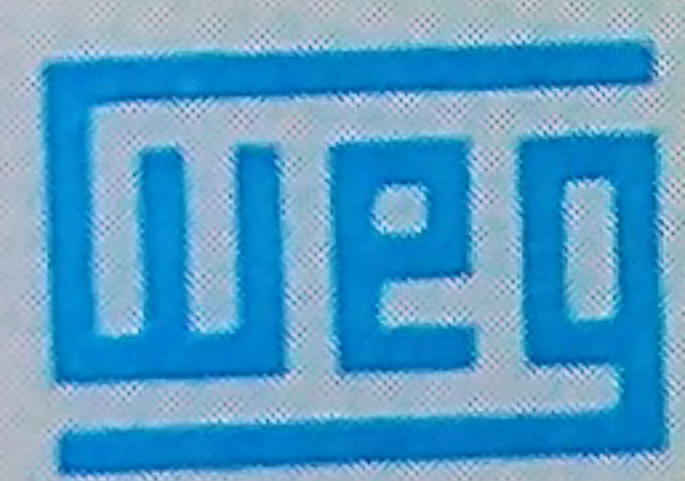

Model # 00318OP3E182JM

Suitable for 208V

SF1.15 FLA 8.96 at 208V

NY127-01 Asset#190917-636 HWP#1

HWP-1-T

CIRCULATING PUMP-HEATING-SEC.

[View motion photo](#)

