Mon 3

ATTACHMENT J-0200000-05
FORMS

CERTIFICATION OF WORK
(To be completed by the Contractor and saved in the Contractor's CMMS)

FACID/Building: PA017-01 Date of Visit: 7/22/2019

Contractor Personnel on Site:

1. TOOCHOCK
2. _____
3. _____
4. _____
5. _____
6. _____

Work Performed:

Preventive Maintenance - Services Completed (Annual, Quarterly, Monthly, equipment identification, etc.)

1. MOSLER BLACK LABEL, PM PER LIST
2. MR302 - HAND
3. NO COMP. CHANGE REQUESTED
4. _____
5. _____
6. _____

To be signed by the Contractor:

Print Name: Technicians Name CRAIG TOOCHOCK Date: 7/22/2019

Signed: _____

To be signed by Facility Manager:

By signing the Certification of Work, the said government representative signature does not constitute acceptance of any work performed by the contractor, it only acknowledges that the contractor was on-site during the identified timeline:

Print Name/Rank: London Leslie Date: 7/22/19

Signed: _____

E-Mail: _____

PREVENTATIVE MAINTENANCE PROGRAM CHECKLIST
VAULT DOOR

SITE AND BLDG #: PA017-01 **MECHANIC SIGNATURE:** [signature] **DATE:** 7/22/2019

LOCATION/RM #: **WO#** 9794 **ASSET #** 7937 **START TIME:** 1055 **FINISH TIME:** 1115

CHECK POINT	CHECKPOINT DESCRIPTION	TASK COMPLETE YES	TASK COMPLETE NO	NOTES/ ACTIONS (IF TASK COMPLETE IS CHECKED NO, PROVIDE EXPLANATION)
	SPECIAL INSTRUCTIONS			
1	In addition to the procedure(s) outlined in this standard, the equipment manufacturer's recommended maintenance procedure(s) and/or instruction(s) shall be strictly adhered.	✓		
2	Follow lock out/tag out procedures at all times. De-energize or discharge all hydraulic, electrical, mechanical, or thermal energy prior to beginning work.	N/A		
	TO BE PERFORMED AT EACH INSPECTION SERVICE			
1	Check alignment of dial ring with lock case; correct if necessary.	✓		
2	Check mounting screws of dial ring and lock case; tighten them, using a thread locking compound.	✓		
3	Look for corrosion or presence of any foreign matter that will in any manner affect the lock's proper operation.	✓		—
4	Look for any signs of malfunctioning or impending failure.	✓		
5	Look for any signs of tampering, forced, or covert entry; report this to the local Security and Law Enforcement Office.	✓		
6	Check Alignment of door with frame	✓		
7	Check for difficulty in opening, closing or locking the door.	✓		
8	Replace all defective hardware	✓		NONE

Note: The technician shall perform any repairs identified during PM up to $250 (direct labor and direct material cost) per PM occurrence. For any deficiencies found exceeding $250 open a corrective maintenance (CM) ticket and include the Asset #, WO #, photos, and a detailed discription of the deficiency.
To be perfomed by: General Maintenance Worker
Additional Notes:

CLOSED
8

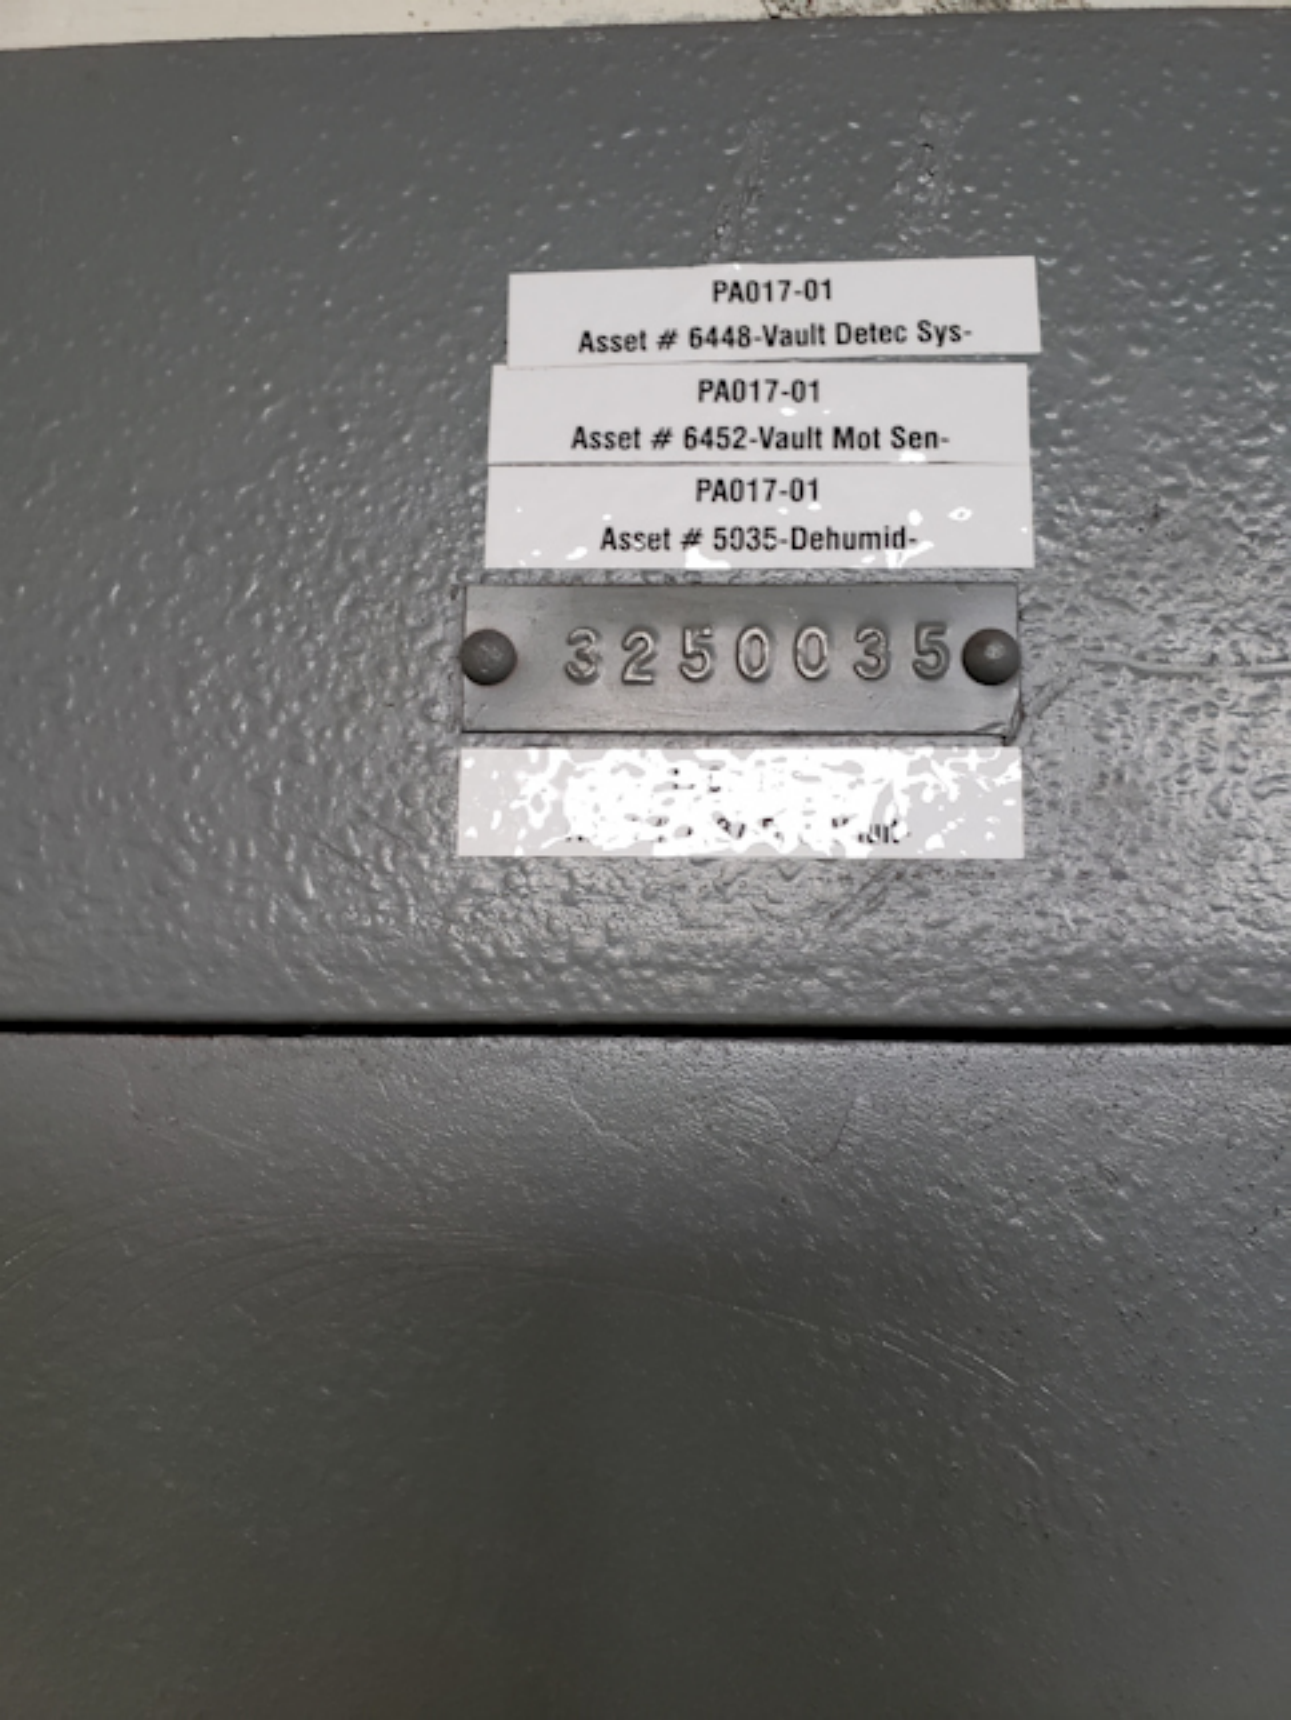
PA017-01
Asset # 6448-Vault Detec Sys-
PA017-01
Asset # 6452-Vault Mot Sen-
PA017-01
Asset # 5035-Dehumid-
3250035
